


Elmer Beach Management Scheme

Construction Phase

Programme – 3 week forward look

- Around 8pm on Saturday 8th August general cargo vessel EDMY will arrive at Elmer. Upon arrival (subject to weather conditions) it will transfer ~ 1/3rd of its load to the transfer barge which will be tugged to shore to discharge its load at high water. It will take three trips in total to discharge the full load. Discharge is expected to be complete within 72hrs
- 10-14th August – The exposed outfall pipe will be removed and the new pipe installed. Construction of the Breakwater extension will commence.
- 17th - 21st August – Piling will commence to encase the new pipe.

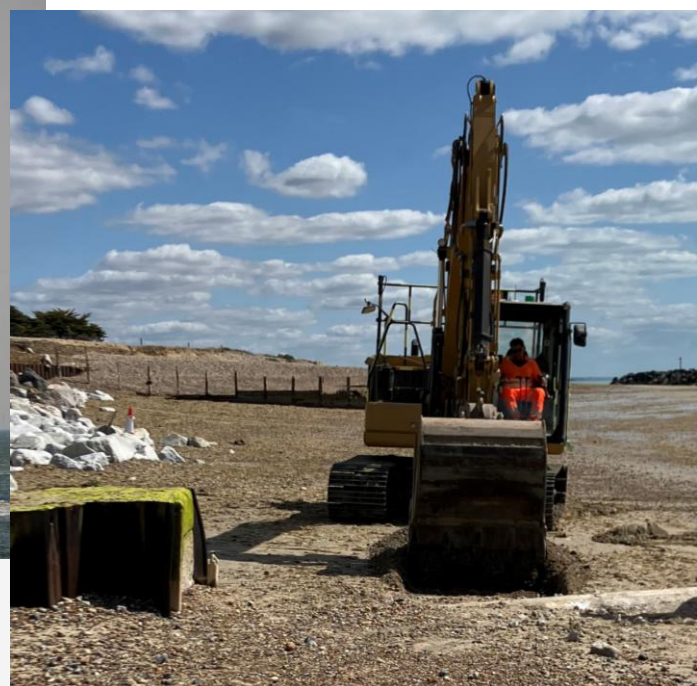

What we have done so far.

- ✓ Site mobilisation and compound set up.
- ✓ CCTV of Elmer Rife outfall pipe
- ✓ Delivery of 90T Excavator and Articulated Dump Truck
- ✓ Excavate to expose pipe and inspect

For more information about the scheme, please contact the East Hampshire and Chichester Asset Performance Team at the Environment Agency on:



03708 506 506

Mon to Fri - 8am to 6pm



Scan the QR code
to send us an email
